HNL TMP Funded Construction Schedule

HONOLULU INTERNATIONAL AIRPORT

TERMINAL MODERNIZATION PROGRAM

PROJECT MANAGEMENT TEAM

Today 03-Feb-10 14:14

Data Date 29-Jan-10

Activity Name	Original Duration	Start	Finish
Construction- 03.003 Elliott St Inter Island Main Fac Site Prep	285	09-Feb-09 A	09-Apr-10
GC Construction-02.001 New Commuter Terminal Phase 1 - Tenant Relocation Improvements	34	08-Mar-10	26-Apr-10
GC Construction-02.002 Bldg Demo/Site Prep Part 1	120	24-May-10	16-Nov-10
GC Construction-02.002 NCT Phase 2 Part 1- Tenant Fit Out	104	26-Jul-10	23-Dec-10
GC Construction-02.002 NCT Phase 2 Part 2 Makai Pier Tenant Fit Out / Escalator	188	26-Jul-10	28-Apr-11
Construction- 03.006 Elliott St. Site Prep for Supp Fac.	210	05-Oct-10	10-Aug-11
Construction- 03.005 Elliott St. Maint. Hangar/Cargo Hawaiian	258	22-Dec-10	06-Jan-12
GC Construction-02.002 Bldg Demo/Site Prep Part 2	107	27-Dec-10	01-Jun-11
DB Construction- 03.001 Elliott St Parking Lot	126	08-Jul-11	09-Jan-12
GC Construction- 03.007 Elliott St Aloha Cargo Demolition	103	21-Jul-11	16-Dec-11
GC Construction 02003 Mauka Concourse-New Mauka Concourse	373	24-Aug-11	25-Feb-13
GC Construction Phase 1- 03.009 Elliott St Taxilanes G&L Widen Phase 1	248	20-Oct-11	18-Oct-12
DB Construction- 03.008 Elliott St Hawaiian/Aloha Bld Demo	200	10-Jan-12	26-Oct-12
GC Construction - 02.006 Mauka Concourse - New Commuter Terminal Phase 3	60	29-Oct-12	28-Jan-13
GC Construction Phase 2- 03.009 Elliott St Taxilanes G&L Widen	146	29-Oct-12	03-Jun-13

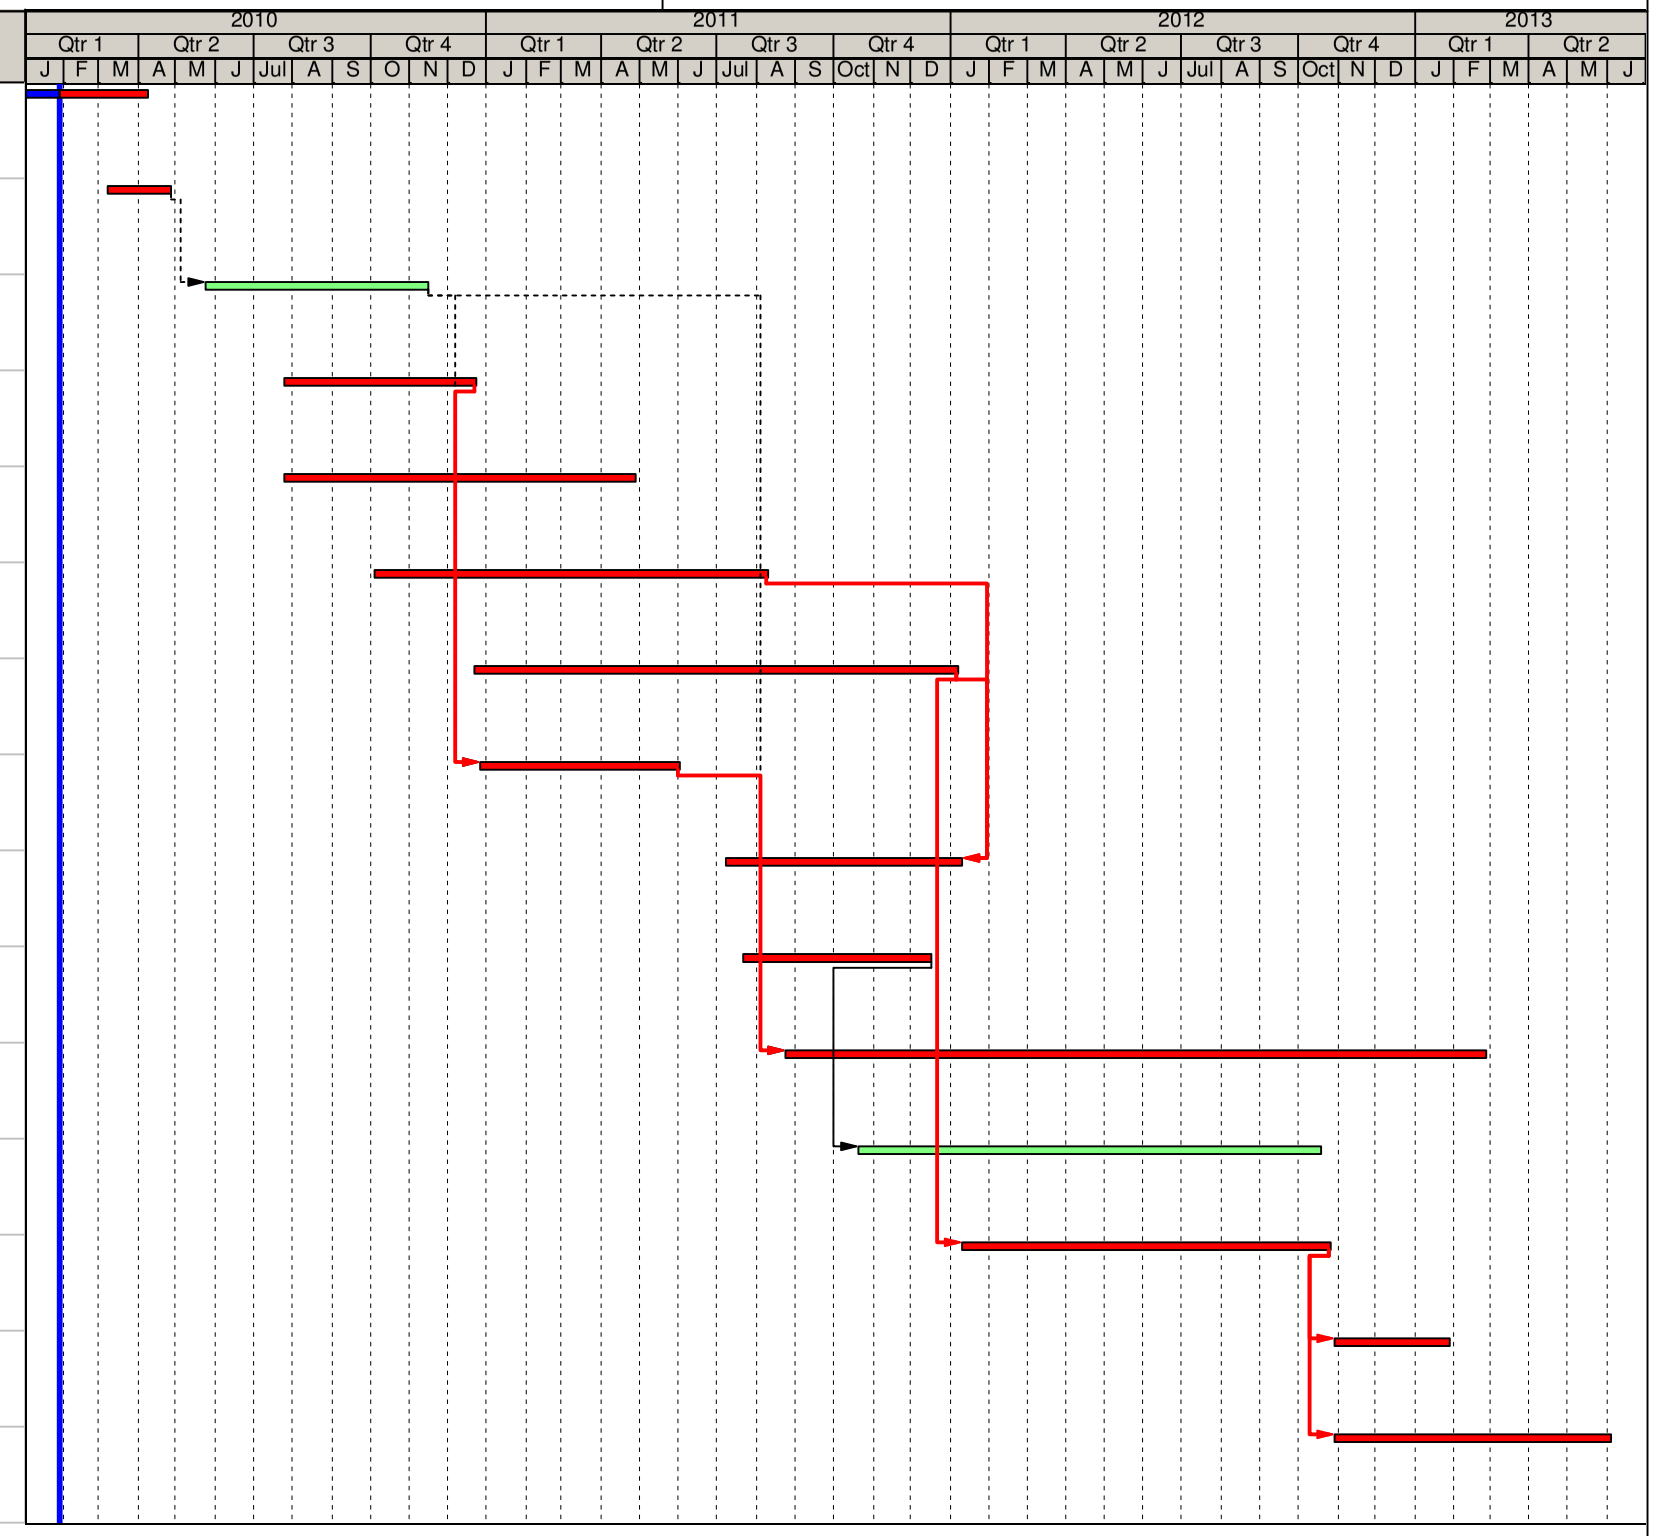

Actual Work
Critical Remaining Work
Remaining Work
Milestone

(c) Primavera Systems, Inc.
